



Broad Street Pedestrian Safety Project

Fact Sheet :

January 10, 2025

What happened this week:

Hard Rock Construction installed temporary traffic control measures along the Broad Street Corridor between Tulane Avenue and the Lafitte Greenway. Through vehicular traffic is now constrained to two travel lanes in each direction.

What is happening next week:

Hard Rock Construction will begin removing sidewalks and driveways along the Broad Street Corridor beginning January 13. Over the next few weeks, crews will remove and replace sidewalks and driveways on the lake side between Conti Street and Iberville Street and along the river side between Tulane Avenue and Palmyra Street. Street parking will not be available while sidewalk work is ongoing. Pedestrian access to businesses will be maintained.



Current timeline: On Track

Questions?



504-905-1561



andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street Pedestrian Safety Project

Fact Sheet :

January 17, 2025

What happened this week:

Hard Rock Construction began removing sidewalks and driveways along the Broad Street Corridor.

What is happening next week:

Over the next few weeks, crews will continue to remove and replace sidewalks and driveways on the lake side between Conti Street and Iberville Street and along the river side between Tulane Avenue and Palmyra Street. Street parking will not be available while sidewalk work is ongoing. Pedestrian access to businesses will be maintained.



Current timeline: On Track

Questions?



504-905-1561



andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street at Bienville Street



Broad Street at Tulane Avenue





Broad Street Pedestrian Safety Project

Fact Sheet :

January 24, 2025

What happened this week:

Due to the extreme weather event that took place this week, crews were slightly delayed. Crews resumed work yesterday and continued today. Crews will be working on Saturday, January 25, to accommodate the lost time.

What is happening next week:

Over the next few weeks, crews will continue to remove and replace sidewalks and driveways on the lake side between Conti Street and Iberville Street and along the river side between Tulane Avenue and Palmyra Street. Street parking will not be available while sidewalk work is ongoing. Pedestrian access to businesses will be maintained.



Current timeline: On Track

Questions?

-  504-905-1561
-  andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



Broad Street at Bienville Street



Broad Street at Tulane Avenue





Broad Street Pedestrian Safety Project

Fact Sheet :

January 30, 2025

What happened this week:

Construction crews have made substantial progress along the lake side between Conti Street and Iberville Street and along the river side between Tulane Avenue and Palmyra Street. Crews have re-paved sidewalks along the lake side between Conti Street and Bienville and along the river side between Tulane Avenue and Banks Street.

What is happening next week:

Over the next few weeks, crews will complete the removal and replacing of sidewalks and driveways on the lake side between Conti Street and Iberville Street and along the river side between Tulane Avenue and Palmyra Street. Street parking will not be available while sidewalk work is ongoing. Pedestrian access to businesses will be maintained. Crews will begin placing traffic detours along the river side from Palmyra to Canal Street and along the lake side from Iberville Street to Canal Street.



Current timeline: On Track

Questions?



504-905-1561



andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street at Banks Street



Broad Street at Conti Street





Broad Street Pedestrian Safety Project

Fact Sheet :

February 7, 2025

What happened this week:

Construction crews have continued to make substantial progress along the lake side between Conti Street and Iberville Street and along the river side between Tulane Avenue and Palmyra Street. Crews have re-paved sidewalks and some driveways along the lake side between Conti Street and Bienville and along the river side between Tulane Avenue and Banks Street.

What is happening next week:

Over the next few weeks, crews will complete the removal and replacing of sidewalks and driveways on the lake side between Conti Street and Iberville Street and along the river side between Tulane Avenue and Palmyra Street. Street parking will not be available while sidewalk work is ongoing. Pedestrian access to businesses will be maintained. Crews will begin placing traffic detours along the river side from Palmyra to Canal Street and along the lake side from Iberville Street to Canal Street.



Current timeline: On Track

Questions?



504-905-1561



andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street at Banks Street



Broad Street at Bienville Street





Broad Street Pedestrian Safety Project

Fact Sheet :

February 14, 2025

What happened this week:

Construction crews have completed sidewalk work along the river side between Tulane Avenue and Banks Street. Traffic detour measures have been removed and the curb ramp at Banks Street has been staged for concrete pouring. Crews have moved along the river side between Palmyra Street and Cleveland Avenue. Traffic detours and temporary sidewalks have been placed and sidewalk removal work has begun. Pedestrian access to businesses will be maintained.

What is happening next week:

Over the next few weeks, crews will complete the removal and replacing of sidewalks and driveways on the lake side between Conti Street and Iberville Street and along the river side between Palmyra Street and Cleveland Avenue. Street parking will not be available while sidewalk work is ongoing. Crews will begin placing traffic detours along the river side from Cleveland Avenue to Canal Street and along the lake side from Iberville Street to Canal Street.



Current timeline: On Track

Questions?



504-905-1561



andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street at Banks Street



Broad Street at Palmyra Street





Broad Street Pedestrian Safety Project

Fact Sheet :

February 21, 2025

Mardi Gras Impacts:

Due to the Endymion Parade on March 1, crews have begun work from Palmyra Street to Tulane Avenue lake side. This is being done to reduce the public safety concerns surrounding the project, and to keep safe flow of foot and vehicular traffic.

What is happening next week:

Over the next few weeks, crews will complete the removal and replacing of sidewalks and driveways on the lake side between Conti Street and Iberville Street and along the river side between Palmyra Street and Cleveland Avenue. Crews will begin work between Palmyra Street to Tulane Avenue lake side. Street parking will not be available while sidewalk work is ongoing. Pedestrian detours have been put in place, along with temporary sidewalks.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement will begin in the coming days.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street from Palmyra to Banks



Broad Street at Banks Street





Broad Street Pedestrian Safety Project

Fact Sheet :

March 14, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Most of the sidewalk work is complete, pending a few curb ramps and driveways.

What is happening next week:

Crews will continue work both riverside and lakeside of Broad St. (US 90) from Cleveland Ave to Iberville St, continuous outside shoulder closures will be in place from Monday, March 17, 2025, to Monday, March 24, 2025, while crews perform work on sidewalks and driveways.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement will begin in the coming days.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street from Iberville Street



Curb Ramp at Banks Street and Broad Street





Broad Street Pedestrian Safety Project

Fact Sheet :

March 21, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Crews have started work between Bienville Street and Iberville Street riverside. Most of the sidewalk work is complete, pending a few curb ramps and driveways.

What is happening next week:

Crews will continue work both riverside and lakeside of Broad St. (US 90) from Cleveland Avenue to Iberville Street, continuous outside shoulder closures will be in place. Crews will continue to place infrastructure for pedestrian signals in major intersections.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement will begin in the coming days.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street at Cleveland Avenue



Banks Street and Broad Street





Broad Street Pedestrian Safety Project

Fact Sheet :

March 28, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Most of the sidewalk work is complete, pending a few curb ramps and driveways.

What is happening next week:

Crews will move into the final phases of removing and replacing sidewalks along the Broad Street Corridor. Continuous outside shoulder closures will be in place. Crews will continue to place infrastructure for pedestrian signals in major intersections.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement will begin in the coming days.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Broad Street at Iberville Street



Banks Street and Canal Street





Broad Street Pedestrian Safety Project

Fact Sheet :

April 4, 2025

Progress:

Crews have moved into the final phases of removing and replacing sidewalks along the Broad Street Corridor. Continuous outside shoulder closures will be in place. Crews will continue to place infrastructure for pedestrian signals in major intersections.

What is happening next week:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Most of the sidewalk work is complete, pending a few curb ramps and driveways. Crews have placed several pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement will begin in the coming days.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Pedestrian Signal (Broad at the Lafitte Greenway)



Pedestrian Signal Conduit (Bienville at Broad Street)





Broad Street Pedestrian Safety Project

Fact Sheet :

April 11, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Most of the sidewalk work is complete, pending a few curb ramps and driveways. Crews have placed several pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Crews will continue to pour concrete for the remaining sidewalks and curb ramps. Hardrock crews will begin the process of patching starting mid week next week. Crews will start inside lane northbound. Milling and Overlay is on schedule to begin the first week of May.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement will begin in the coming days.

Questions?

 504-905-1561

 andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Concrete pouring at Cleveland Ave. and Broad St.



Cleveland Ave. at Broad St.





Broad Street Pedestrian Safety Project

Fact Sheet:

April 25, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is mostly complete, pending a few curb ramps and driveways. Crews have placed several pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Hard Rock crews have begun the process of patching certain areas along the Broad Street Corridor. Milling and Overlay is on schedule to begin the first week of May.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement will begin in the coming days.

Questions?



504-905-1561



andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Palmyra St. at Broad St. River Side.



Iberville St. at Broad St.





Broad Street Pedestrian Safety Project

Fact Sheet :

May 2, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have placed pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Hard Rock crews have continued the process of asphalt patching certain areas along the Broad Street Corridor. Milling and Overlay is on schedule to begin the first week of May.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



Cleveland Ave. at Broad St. River Side.



Iberville St. at Broad St.





Broad Street Pedestrian Safety Project

Fact Sheet:

May 9, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have placed pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Hard Rock crews will continue the process of asphalt patching certain areas along the Broad Street Corridor. Crews have begun removing median cross walks, crews will replace them with ADA compliant ramps. Milling and overlaying has been pushed back to the second week of May. Crews will begin this process in the night time hours.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

Questions?



504-905-1561



andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Cleveland Ave. at Broad St.



Cleveland Ave. at Broad St.





Broad Street Pedestrian Safety Project

Fact Sheet :

May 19, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have placed pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Hard Rock crews will continue the process of asphalt patching certain areas along the Broad Street Corridor. Crews will continue removing median cross walks, and has replaced some crosswalks with ADA compliant ramps. Boh Brothers will begin milling the low lane on both sides of the road Tuesday night (5/20/2025). On Wednesday night, crews will work on the middle lanes and some turnouts. The high lane will be finished Thursday night. Hard Rock will then inspect for any new patches needed before overlaying.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



New Crosswalk at Broad and Banks St.



Patching at Broad St and Cleveland Ave





Broad Street Pedestrian Safety Project

Fact Sheet:

April 25, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is mostly complete, pending a few curb ramps and driveways. Crews have placed several pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Hard Rock crews have begun the process of patching certain areas along the Broad Street Corridor. Milling and Overlay is on schedule to begin the first week of May.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement will begin in the coming days.

Questions?



504-905-1561



andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Palmyra St. at Broad St. River Side.



Iberville St. at Broad St.





Broad Street Pedestrian Safety Project

Fact Sheet :

May 23, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have placed pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Crews will continue removing median cross walks, and has replaced some crosswalks with ADA compliant ramps. Boh Brothers began milling the low lane on both sides of the road on Tuesday night (5/20/2025). Crews will continue to work on the middle lanes and some turnouts. Milling will conclude on Tuesday night (5/27/2025). Hard Rock will then inspect for any new patches needed before overlaying. Crews will not conduct work Monday (5/26/2025) due to the Memorial Day Holiday.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Crosswalk at Canal St. and Broad St.



Milling Work on Broad St.





Broad Street Pedestrian Safety Project

Fact Sheet :

May 2, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have placed pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Hard Rock crews have continued the process of asphalt patching certain areas along the Broad Street Corridor. Milling and Overlay is on schedule to begin the first week of May.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



Cleveland Ave. at Broad St. River Side.



Iberville St. at Broad St.





Broad Street Pedestrian Safety Project

Fact Sheet:

May 9, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have placed pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Hard Rock crews will continue the process of asphalt patching certain areas along the Broad Street Corridor. Crews have begun removing median cross walks, crews will replace them with ADA compliant ramps. Milling and overlaying has been pushed back to the second week of May. Crews will begin this process in the night time hours.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

Questions?



504-905-1561



andrew.logan@nola.gov


Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



Cleveland Ave. at Broad St.

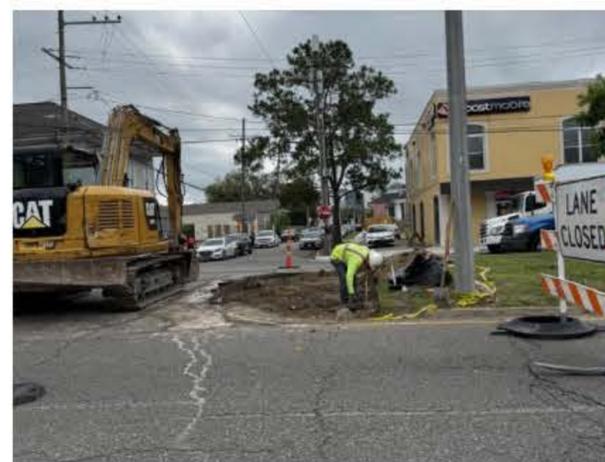

Cleveland Ave. at Broad St.





Broad Street Pedestrian Safety Project

Fact Sheet :

May 19, 2025

Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have placed pedestrian signal conduits, and have begun construction on a pedestrian signal at the Lafitte Greenway and Broad Street.

What is happening next week:

Hard Rock crews will continue the process of asphalt patching certain areas along the Broad Street Corridor. Crews will continue removing median cross walks, and has replaced some crosswalks with ADA compliant ramps. Boh Brothers will begin milling the low lane on both sides of the road Tuesday night (5/20/2025). On Wednesday night, crews will work on the middle lanes and some turnouts. The high lane will be finished Thursday night. Hard Rock will then inspect for any new patches needed before overlaying.



Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:
nola.gov/publicworks



City of New Orleans
Mayor LaToya Cantrell



New Crosswalk at Broad and Banks St.



Patching at Broad St and Cleveland Ave

