



# Broad Street Pedestrian Safety Project

## Fact Sheet :

June 13, 2025

### Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have completed asphalt work along the corridor. Crews have completed the installation of two traffic arm mast at the Lafitte Greenway, and will complete the installation of traffic signals in the coming weeks. When complete these will serve as a pedestrian hybrid beacon.

### What is happening next week:

Crews will continue replacing the final crosswalks making them ADA accessible. Crews expect road work to be completed by the end of June, including completed turn around intersections and new pavement striping along the corridor. Pedestrian signals along Broad are set to be completed by the end of July. Proper signage is in place for drivers visibility.



### Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

#### Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**  
Mayor LaToya Cantrell



Traffic Arm Mast at Lafitte Greenway



Broad St. at Palmyra St.





# Broad Street Pedestrian Safety Project

## Fact Sheet :

June 20, 2025

### Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have completed asphalt work along the corridor. Crews have completed the installation of two traffic arm mast at the Lafitte Greenway, and will complete the installation of traffic signals in the coming weeks. When complete these will serve as a pedestrian hybrid beacon.

### What is happening next week:

Curb work in the median along Broad Street has been completed, and as a result, an additional lane is scheduled to reopen by early next week. New traffic signal equipment is expected to arrive during the first week of July, marking another key milestone in finalizing the corridor improvements. Pavement striping is tentatively scheduled, pending feedback and decisions made during the upcoming community meeting on June 26.



### Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

#### Questions?

504-905-1561

andrew.logan@nola.gov

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**  
Mayor LaToya Cantrell



Broad St. at Bienville St.



Broad St. at Palmyra St.





# Broad Street Pedestrian Safety Project

## Fact Sheet :

August 1, 2025

### What is happening next week:

All pedestrian signals, except for the Pedestrian Hybrid Beacon at the Lafitte Greenway, will be activated next week. Striping along the corridor is expected to begin within the next two weeks, and the beacon at the Greenway will be turned on once that work is complete. Project completion is still anticipated by the end of August.



### Current timeline: End of August



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

#### Questions?



504-905-1561



[andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**  
Mayor LaToya Cantrell



Broad St. at Bienville St.



Broad St. at Lafitte Greenway





# Broad Street Pedestrian Safety Project

## Fact Sheet :

August 15, 2025

### What is happening next week:

All pedestrian signals along the Broad Street corridor have now been activated, with the exception of the Pedestrian Hybrid Beacon at the Lafitte Greenway. Striping work is scheduled to begin in the coming weeks, and once that is complete, the hybrid beacon will be turned on. The project remains on schedule, with completion still anticipated by the end of August.



### Current timeline: End of August



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

#### Questions?



504-905-1561



[andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)


Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**  
Mayor LaToya Cantrell



Broad St. at Bienville St.

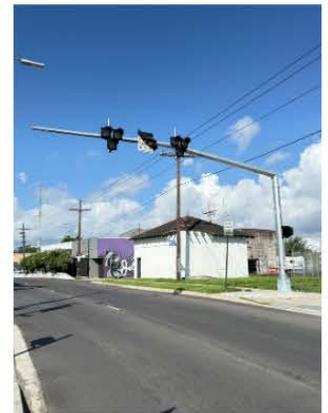

Broad St. at Lafitte Greenway





# Broad Street Pedestrian Safety Project

## Fact Sheet :

September 2, 2025

### What is happening next week:

Hard Rock Construction’s paving subcontractor is scheduled to return next week to complete final leveling course adjustments at ADA ramps along the Broad Street corridor. Once this work is finished, the striping subcontractor will mobilize to install final pavement markings, including crosswalk striping. Following striping, crews will proceed with activating the new Pedestrian Hybrid Beacon at the Lafitte Greenway crossing on North Broad. This is the most up-to-date information available, and the project team remains confident that the Broad Street Pedestrian Improvement Project will be completed within the next two weeks.



### Current timeline: Fall 2025



#### Questions?

 504-905-1561

 [andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)

The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.



**City of New Orleans**  
Mayor LaToya Cantrell





# Broad Street Pedestrian Safety Project

## Fact Sheet :

June 27, 2025

### Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have completed asphalt work along the corridor. Crews have completed the installation of two traffic arm mast at the Lafitte Greenway, and will complete the installation of traffic signals in the coming weeks. When complete these will serve as a pedestrian hybrid beacon. LADOTD hosted a successful community meeting on 6/26/2025.

### What is happening next week:

Traffic has opened to two lanes. Traffic will be restricted to two lanes while DOTD prepares to install final roadway striping. Remaining traffic signal equipment is expected to arrive the first week of July, at which time crews will begin installing the remaining pedestrian countdown signals at intersections.



## Current timeline: On Track

### Questions?

 504-905-1561

 [andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**

Mayor LaToya Cantrell



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.





# Broad Street Pedestrian Safety Project

## Fact Sheet :

July 11, 2025

### Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have completed asphalt work along the corridor. All ADA crosswalks have been completed, including curb work. Crews have completed the installation of two traffic arm mast at the Lafitte Greenway, and will complete the installation of traffic signals in the coming weeks. When complete these will serve as a pedestrian hybrid beacon.

### What is happening next week:

Crews have begun installing pedestrian countdown signal equipment at intersections along the corridor between the Lafitte Greenway and Tulane Avenue. Most signal poles have been installed pending a few more along the corridor. Traffic will remain restricted to two lanes while DOTD prepares to install final roadway striping. This project is slated to be completed by the end of July.



### Current timeline: On Track



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

#### Questions?

 504-905-1561

 [andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**  
Mayor LaToya Cantrell



Broad St. at Bienville St.



Broad St. at Lafitte Greenway





# Broad Street Pedestrian Safety Project

## Fact Sheet :

July 25, 2025

### Progress:

Crews have made significant progress along the Broad Street corridor between Conti Street and Tulane Avenue. Sidewalk work is complete along the corridor. Crews have completed asphalt work along the corridor. All ADA crosswalks have been completed, including curb work. Crews have completed the installation of two traffic arm mast at the Lafitte Greenway, and will complete the installation of traffic signals in the coming weeks. When complete these will serve as a pedestrian hybrid beacon.

### What is happening next week:

Crews have successfully completed all sidewalk work, ADA curb ramps, as well as milling and overlaying along the corridor. Installation of pedestrian signals is now underway, including a pedestrian hybrid beacon at the Lafitte Greenway to enhance safety and accessibility.

Pending final decisions from the Louisiana Department of Transportation and Development (DOTD), the project timeline has been extended. We now anticipate full completion by the end of August.



### Current timeline: End of August



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.

#### Questions?

504-905-1561

andrew.logan@nola.gov


Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**  
Mayor LaToya Cantrell



Broad St. at Bienville St.

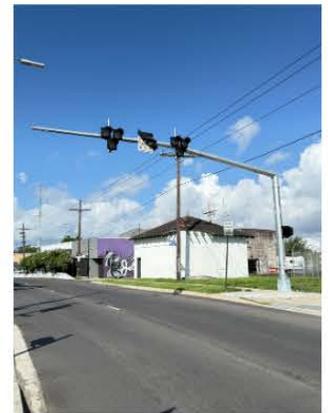

Broad St. at Lafitte Greenway





# Broad Street Pedestrian Safety Project

## Fact Sheet :

October 17, 2025

### What is happening next week:

We'd like to provide an update on the Broad Street Pedestrian Improvement Project. As part of the recent work along Broad Street between Tulane Avenue and the Lafitte Greenway, crews are currently awaiting delayed signage needed for the Pedestrian Hybrid Beacon at the Greenway. The supplier expects delivery within the next 30 days, after which crews will promptly install the signage and activate the beacon.



### Current timeline: Fall 2025



#### Questions?

 504-905-1561

 [andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.





# Broad Street Pedestrian Safety Project

## Fact Sheet:

November 7, 2025

### What is happening this week:

We are excited to announce that the signage for the Pedestrian Hybrid Beacon at the Lafitte Greenway has arrived and been installed, and the beacon is now fully activated. The Broad Street Pedestrian Improvement Project is in its preliminary completion phase and will be finalized following walk-through inspections of the corridor.



### Current timeline: Fall 2025



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.



### Questions?

📞 504-905-1561

✉️ [andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**  
Mayor LaToya Cantrell





# Broad Street Pedestrian Safety Project

## Fact Sheet :

September 8, 2025

### What is happening next week:

Hard Rock's subcontractor milled the pavement before and after the ramps to create a smooth transition, since the median ramps are higher because of the box culvert. Both lanes had to be milled to keep the cross slope consistent as traffic comes off the median. The issue has been resolved and striping is scheduled to begin on September 16th.



### Current timeline: Fall 2025



#### Questions?

 504-905-1561

 [andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)

The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.



**City of New Orleans**  
Mayor LaToya Cantrell





# Broad Street Pedestrian Safety Project

## Fact Sheet :

September 15, 2025

### What is happening next week:

Beginning tomorrow, September 16, the Hard Rock crew will begin striping Broad Street from Tulane Avenue to the Lafitte Greenway. During this work, motorists should expect lane closures on both the river-bound and lake-bound sides. Striping is anticipated to take approximately 2-3 days to complete. Once this phase is finished, the Pedestrian Hybrid Beacon at the Lafitte Greenway will be activated, further enhancing safety and accessibility for everyone using the corridor.



### Current timeline: Fall 2025



#### Questions?

 504-905-1561

 [andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.





# Broad Street Pedestrian Safety Project

## Fact Sheet:

September 23, 2025

### What is happening next week:

Last week, Hard Rock crews began installing roadway striping along the Broad Street corridor between Tulane Avenue and the Lafitte Greenway. Work will continue this week to complete striping throughout the project area. Once this phase is finished, the Pedestrian Hybrid Beacon at the Lafitte Greenway will be activated to enhance pedestrian safety.



### Current timeline: Fall 2025



The Department of Public Works reminds residents and business owners to refrain from parking on the sidewalks, parking enforcement has been notified, and enforcement has begun.



#### Questions?

📞 504-905-1561

✉️ [andrew.logan@nola.gov](mailto:andrew.logan@nola.gov)

Visit our project page:  
[nola.gov/publicworks](http://nola.gov/publicworks)



**City of New Orleans**  
Mayor LaToya Cantrell

